

Revised Construction Staging

Project: Middlesex Turnpike, Phase II

Location: Bedford/Burlington/Billerica, MA

Contract No: MassDOT 63316

Contractor: Newport Construction Corp.

Location of Work: Middlesex Turnpike - MITRE Link to Plank Street/Crosby Drive Intersection
400+00 to 445+00 Main Line

Description of Work: Construction of roadway including utility installation of remaining portion
(existing roadway area)

Work Zones: Phase 1 – Plank Street/Crosby Drive Intersection to Doubletree/Hampton Inn
intersection – 445+00 to 421+00

Phase 2 – Doubletree/Hampton Inn Intersection to MITRE Link – 421+00 to
400+00

Special Conditions Widening on baseline right will be utilized by utility companies to relocate
utilities.

Widening on baseline left must be completed to binder grade with granite curb
and cement concrete sidewalks to be utilized for one-way southbound traffic.

Phase 1 – 445+00 to 421+00

Traffic Control One way traffic through phase, Plank Street/Crosby Drive (PS/CD) intersection
to just before Doubletree/Hampton Inn (D/HI) intersection. Two way traffic
from D/HI to Bedford Street.

Detour Crosby Drive will be the detour, southbound traffic only through work zone.

Message Boards Burlington Street before Crosby Drive
Bedford Street across from Network Drive
Middlesex Turnpike at Bedford Street
Middlesex Turnpike at Plank Street

Special Conditions Access through work zone for 55 Middlesex Turnpike


Type of Work Remove and dispose of existing pavement
Install drainage
Construct roadway up to bituminous concrete binder course

Duration 10 Weeks

Phase 2 – 421+00 to 404+00

Traffic Control	One way traffic through phase, Doubletree/Hampton Inn (D/HI) intersection to MITRE Link. Two way traffic from PS/CD to D/HI. Two way traffic from Bedford Street to Crowley Road.
Detour	Crosby Drive will be the detour, southbound traffic only through work zone.
Message Boards	Burlington Street before Crosby Drive Bedford Street across from Network Drive Middlesex Turnpike at Bedford Street Middlesex Turnpike at Plank Street
Special Conditions	Need to utilize MITE Link to run southbound traffic Burlington and Bedford must complete sidewalks as required before MITRE Link can be opened. Traffic Signals must be completed at Network Drive & MITTE Link & Bedford Street. Will close Middlesex Turnpike at Crowley Road 12" water connection at Rte. 62 must be completed. MITRE radar facility driveway and swale must be completed
Type of Work	Remove and dispose of existing pavement Install drainage Construct roadway up to bituminous concrete binder course
Duration	10 Weeks

To see all the details that are visible on the screen use the Print link next to the map

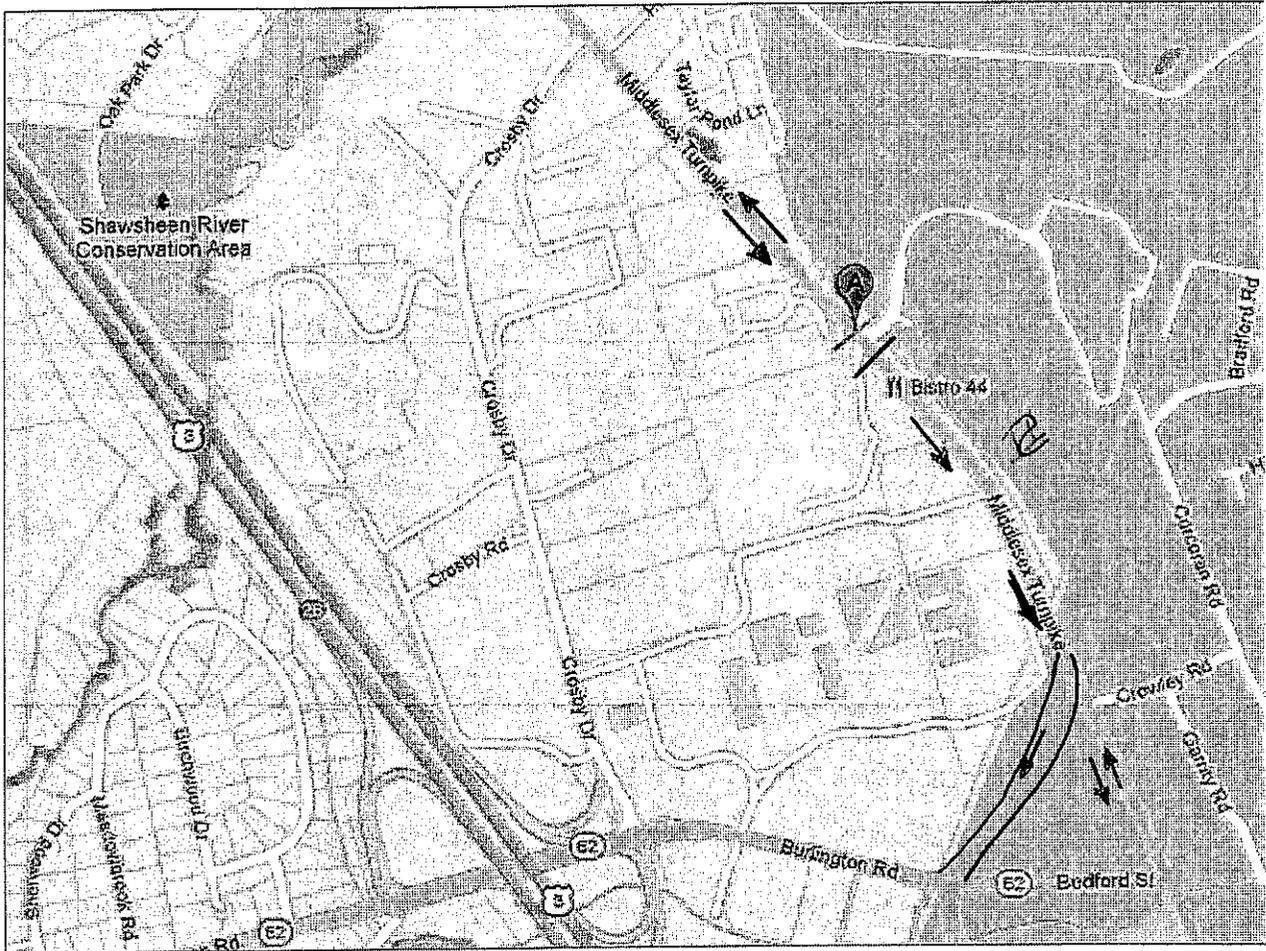

Work ZONE E - 10 weeks

- Doubletree / Hampton to Crowley ROAD
 - 2-way TRAFFIC PLANK to HOTELS
 - SB TRAFFIC ONLY Beyond HOTELS
 - Run SB Through New Roadway (MILWAUKEE)
 - 2-way traffic RT 62 (BRIDGEMAN ST) to Crowley Rd
 - NO ACCESS THRU WORK ZONE FOR BRT
- BLT-40
 - 36
 - MITRE
- CONSTRUCT DRAINAGE & ROADWAY

- Needs SW's By Bedford & Burlington Done

- Signals @ Network Drive
- PUNT MARKINGS
- 12" water crossing on 62
- Driveway
- SWALE
