WILSON MILL DAM
PRELIMINARY BASELINE SCHEDULE

ID		Task Name	Duration	Start	Finish
1		Notice to Proceed	0 days	Mon 4/30/12	Mon 4/30/12
2		Mobilize, Install Signage Etc	1 day	Mon 4/30/12	Tue 5/1/12
3		Cleaning	2 days	Tue 5/1/12	Thu 5/3/12
4		Erosion Control	1 day	Thu 5/3/12	Fri 5/4/12
5		Grubbing/Fencing/Tree Protection	1 day	Fri 5/4/12	Mon 5/7/12
6		Remove Existing Headwall/Primary Stoplogs	1 day	Thu 5/3/12	Fri 5/4/12
7		Clear overflow culvert for lining	1 day	Fri 5/4/12	Mon 5/7/12
8		Gas Line Abandonment	5 days	Mon 5/7/12	Mon 5/14/12
9		Install 16" (open left) butterfly gate	2 days	Mon 5/14/12	Wed 5/16/12
10		Install Water line by-pass/chonnate/test/connect	5 days	Tue 5/15/12	Tue 5/22/12
11		Install/Grout 36" HDPE overflow liner	15 days	Mon 5/14/12	Tue 6/5/12
12		Install turbidity boom	1 day	Mon 5/21/12	Tue 5/22/12
13		Construct Canoe Launch	10 days	Mon 5/21/12	Tue 6/5/12
14		Backfill Downstream Overflow Extension	3 days	Tue 6/5/12	Fri 6/8/12
15		Grade Access for Walls 3,4,5	2 days	Fri 6/8/12	Tue 6/12/12
16					
17		PHASE 1	0 days	Tue 6/12/12	Tue 6/12/12
18		Install Water Control Phase 1	4 days	Tue 6/12/12	Mon 6/18/12
19		Excavate/Prep for Spillway	3 days	Mon 6/18/12	Thu 6/21/12
20		Excavate/Place Concrete Cutoff	2 days	Thu 6/21/12	Mon 6/25/12
21		Form/Rebar/Place Spillway Footing	3 days	Mon 6/25/12	Thu 6/28/12
22		Form/Rebar/Place Spillway Walls	5 days	Thu 6/28/12	Fri 7/6/12
23		Form/Rebar/Place Auxiliary Spillway Section	5 days	Fri 7/6/12	Fri 7/13/12
24		Form/Rebar/Pour Cutoff Wall	3 days	Fri 7/13/12	Wed 7/18/12
25		Prep/Stone Base Spillway Apron	2 days	Tue 7/10/12	Thu 7/12/12
26		Form/Rebar/Pour Spillway Apron	4 days	Thu 7/12/12	Wed 7/18/12
27		Strip/Prep for stonework	3 days	Wed 7/18/12	Mon 7/23/12
28		Install stone Veneer Spillway	7 days	Mon 7/23/12	Wed 8/1/12
29		Install Wilson Mill Stone Apron Facing	3 days	Tue 7/31/12	Fri 8/3/12
30		Grout Apron Stone Facing	1 day	Fri 8/3/12	Mon 8/6/12
31					
32		Pressure Inject Grout Primary Spillway	5 days	Mon 6/25/12	Mon 7/2/12
33		Install Rebar/Form/Place Wall #1 and #2	8 days	Mon 7/2/12	Fri 7/13/12
34		Map/Demo/Store Existing Headwalls at Primary Spillway	6 days	Fri 7/13/12	Mon 7/23/12
35		Excavate, Remove Existing Arch Primary Spillway	3 days	Mon 7/23/12	Thu 7/26/12
36		Set New Pre-Cast Arch for Primary Culvert	2 days	Thu 7/26/12	Mon 7/30/12
37		Backfill Primary Spillway Arch	3 days	Fri 7/27/12	Wed 8/1/12
38		Reconstruct Stone Headwalls Primary Arch	10 days	Wed 8/1/12	Wed 8/15/12
39					
40		Excavate/Prep/Pour Footing Wall #4	2 days	Mon 6/18/12	Wed 6/20/12
41		Construct Wall #4	8 days	Wed 6/20/12	Mon 7/2/12
42		Reconstruct Wall #3	8 days	Mon 7/2/12	Fri 7/13/12
43		Excavate/Prep/Pour Footing Wall #5	2 days	Fri 7/13/12	Tue 7/17/12
44		Construct Wall #5	20 days	Mon 7/23/12	Mon 8/20/12
45					
46		Install Water Control At Wall #6	3 days	Mon 8/6/12	Thu 8/9/12

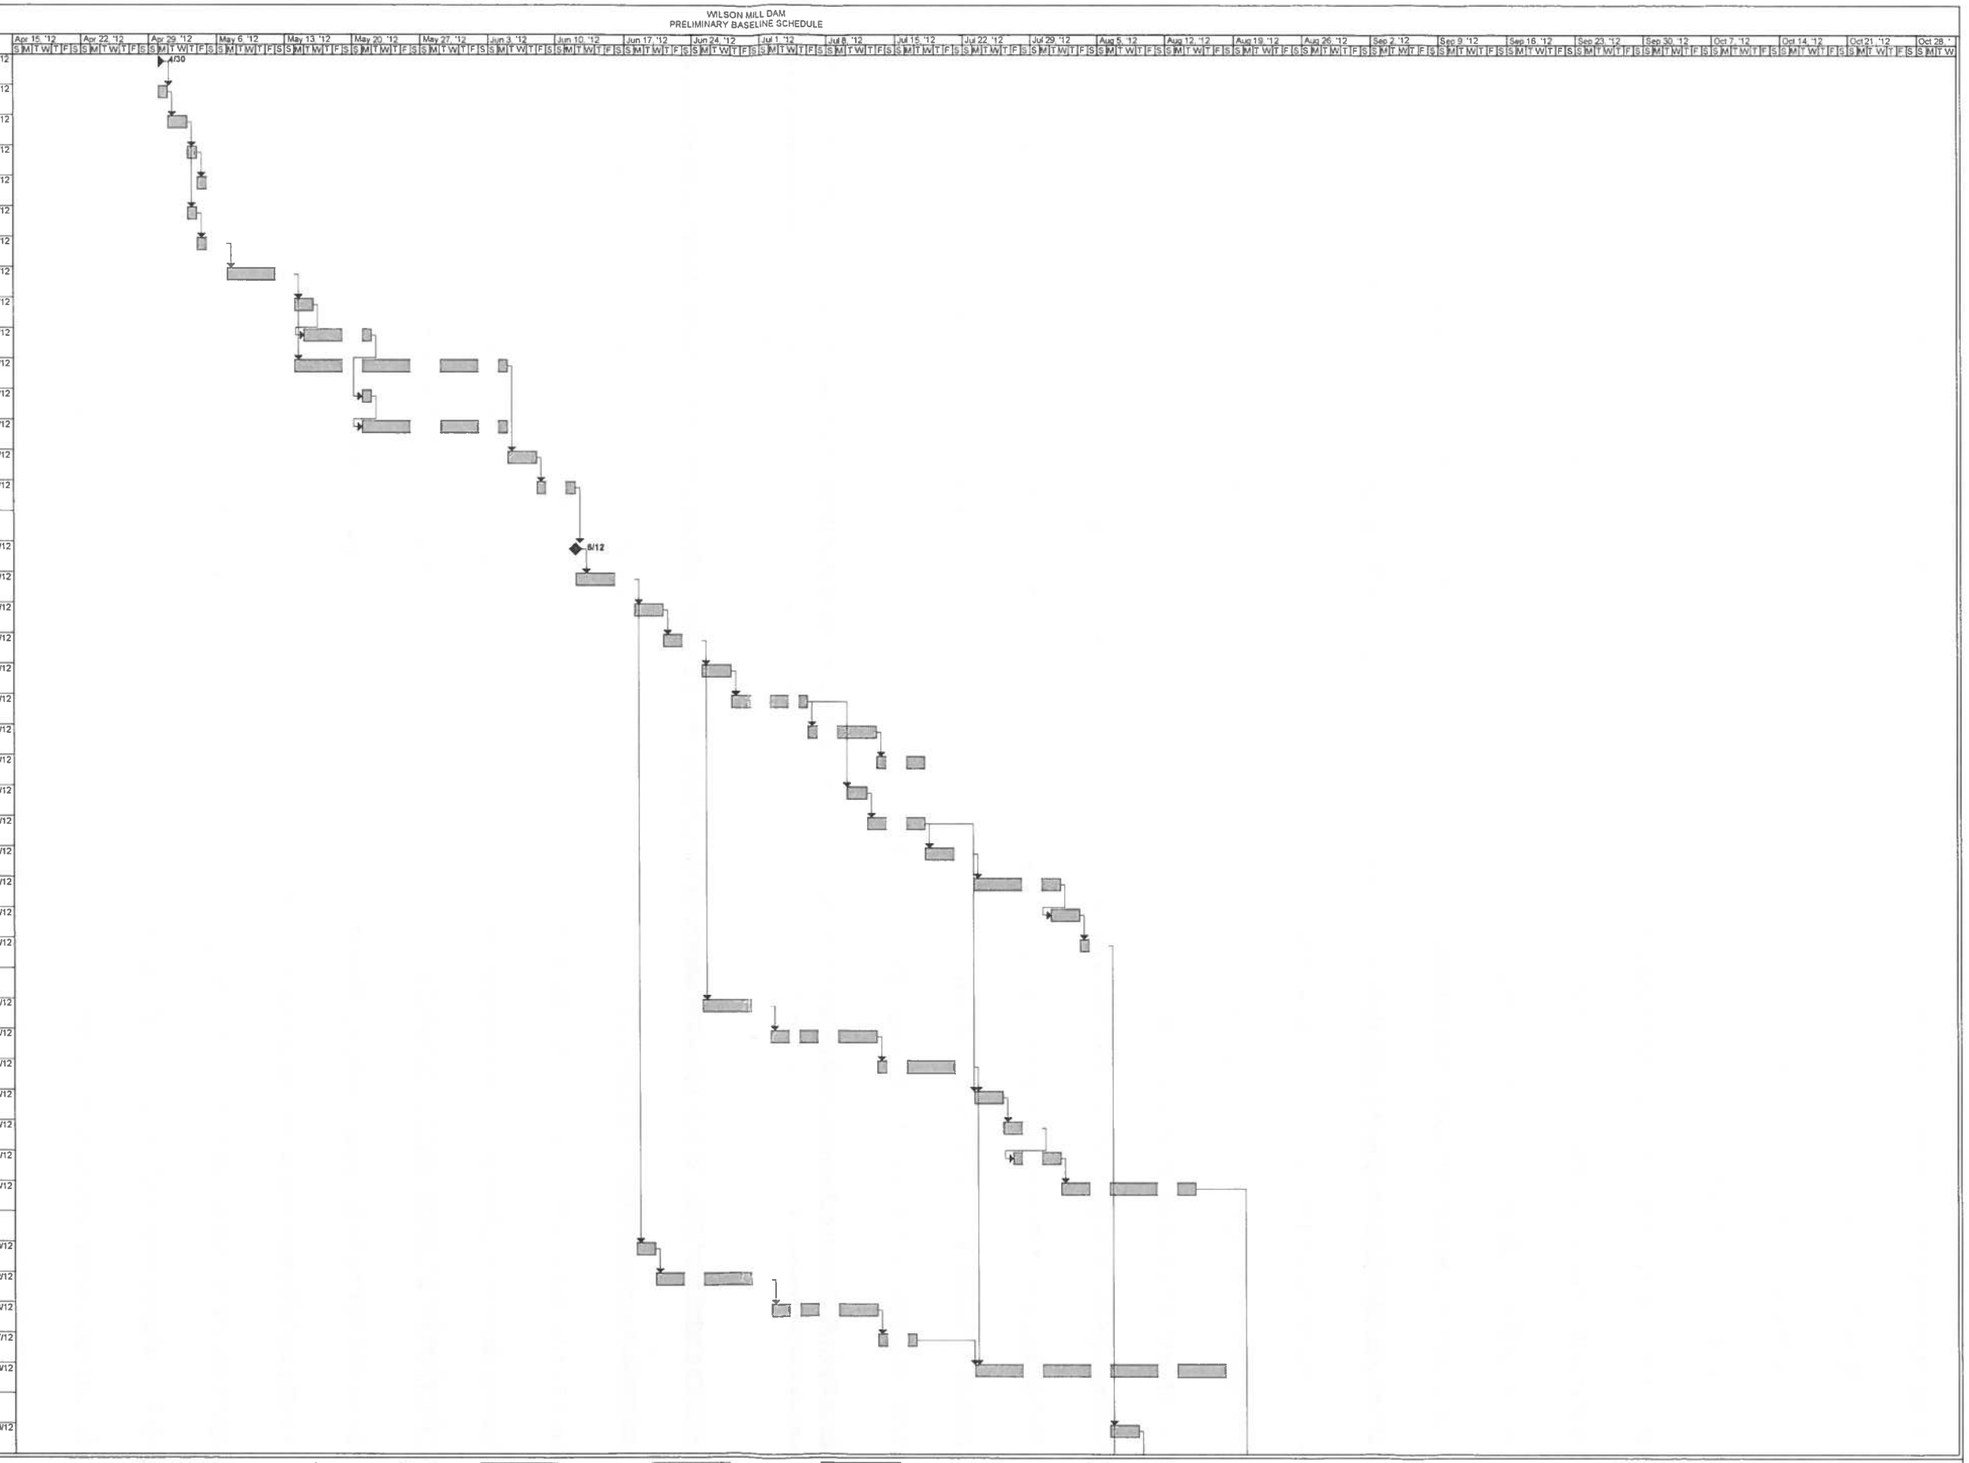

Project: Wilson Mill Dam Baseline Sch
Date Mon 4/2/12

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline

WILSON MILL DAM
PRELIMINARY BASELINE SCHEDULE

ID		Task Name	Duration	Start	Finish
47		Excavate/Prep Base Wall #6	1 day	Thu 8/9/12	Fri 8/10/12
48		Form/Rebar/Place Footing Wall #6	2 days	Thu 8/9/12	Mon 8/13/12
49		Form/Rebar/Pour Wall #6	5 days	Mon 8/13/12	Mon 8/20/12
50		Stone Veneer Wall #6	5 days	Mon 8/20/12	Mon 8/27/12
51					
52		PHASE 2	0 days	Mon 4/16/12	Mon 4/16/12
53		Reconfigure Water Controls to Phase 2	3 days	Mon 8/6/12	Thu 8/9/12
54		Excavate/Prep for Spillway	2 days	Thu 8/9/12	Mon 8/13/12
55		Excavate/Place Concrete Cutoff	2 days	Fri 8/10/12	Tue 8/14/12
56		Form/Rebar/Place Spillway Footing	2 days	Tue 8/14/12	Thu 8/16/12
57		Form/Rebar/Place Concrete Spillway Walls	5 days	Thu 8/16/12	Thu 8/23/12
58		Form/Rebar/Place Left Buttress	4 days	Thu 8/23/12	Wed 8/29/12
59		Form/Rebar/Place Left Cutoff Wall	3 days	Wed 8/29/12	Tue 9/4/12
60		Prep Stone Base for Spillway Apron	2 days	Tue 9/4/12	Thu 9/6/12
61		Form/Rebar/Pour Spillway Apron	3 days	Thu 9/6/12	Tue 9/11/12
62		Install Stone Veneer Spillway	5 days	Tue 9/11/12	Tue 9/18/12
63		Install Wilson Mill Stone Apron Facing	3 days	Tue 9/18/12	Fri 9/21/12
64		Grout Apron Stone Facing	1 day	Fri 9/21/12	Mon 9/24/12
65					
66		Construct Overflow Culvert Stone Headwall	4 days	Mon 8/27/12	Fri 8/31/12
67		Construct Overflow Headwall Splash Pad	3 days	Fri 8/31/12	Thu 9/6/12
68		Backfill, Grading, Sediment Forebay. Loam/Seed	8 days	Thu 9/6/12	Tue 9/18/12
69					
70		**Remove Water Controls / Restore Flows**	2 days	Mon 9/24/12	Wed 9/26/12
71					
72		ROADWAY AND LANDSCAPING	0 days	Mon 4/16/12	Mon 4/16/12
73		Restore Water Line	3 days	Wed 9/26/12	Mon 10/1/12
74		Restore Gas Line	5 days	Mon 10/1/12	Mon 10/8/12
75		Construct 30" Stone Wall Sample	3 days	Mon 10/1/12	Thu 10/4/12
76		Construct 30" Stone Wall	6 days	Thu 10/4/12	Fri 10/12/12
77		Excavate/Form/Place Railing Footings	3 days	Mon 10/8/12	Thu 10/11/12
78		Install Granite Curb	3 days	Thu 10/11/12	Tue 10/16/12
79		Restore Site Amenities	1 day	Tue 10/16/12	Wed 10/17/12
80		Stone Dust Walkways	1 day	Tue 10/16/12	Wed 10/17/12
81		Subgrade Roadway and Gravel Parking Area	3 days	Tue 10/16/12	Fri 10/19/12
82		Pave Driveway and Roadway	1 day	Fri 10/19/12	Mon 10/22/12
83		Install Wall #3 Fencing	1 day	Mon 10/22/12	Tue 10/23/12
84		Install Railing	3 days	Tue 10/23/12	Fri 10/26/12
85		Site cleanup and demobe	3 days	Wed 10/24/12	Mon 10/29/12

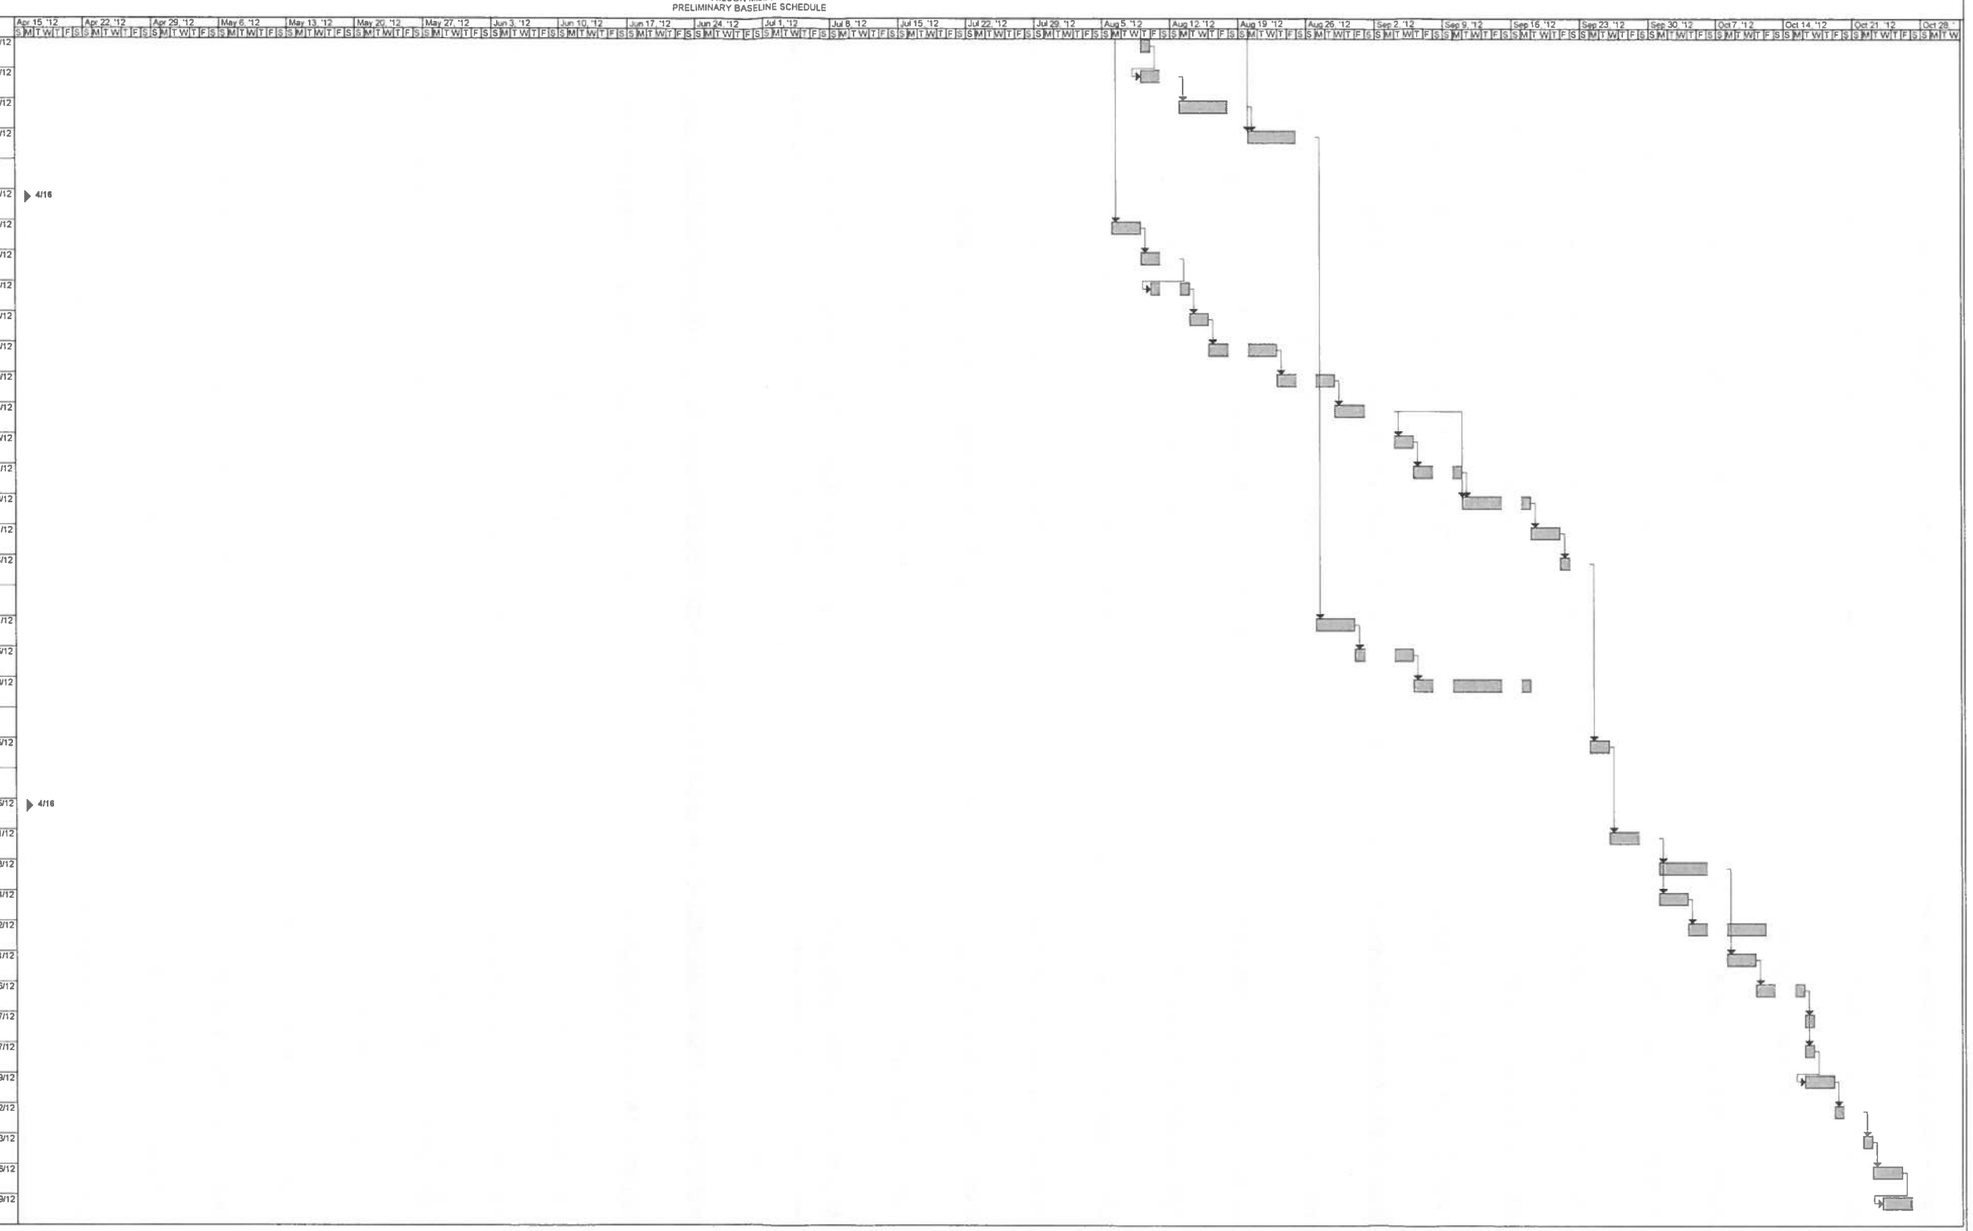

Project: Wilson Mill Dam Baseline Sch
Date Mon 4/2/12

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline
